


Executive schedule assessment

Status: 2026-09-18 | Fictional, unclassified portfolio demonstration

Acceptance forecast: 2027-09-21. The deterministic forecast is 18 workdays later than the 2027-08-26 approved baseline. The risk model places P50 at **2027-10-08** and P80 at **2027-10-14**.

The schedule contains 152 leaf activities and milestones, 224 dependency links and six resource pools. 78 items are complete. 66 unfinished items have zero network float. 16 future or missed milestones require attention.

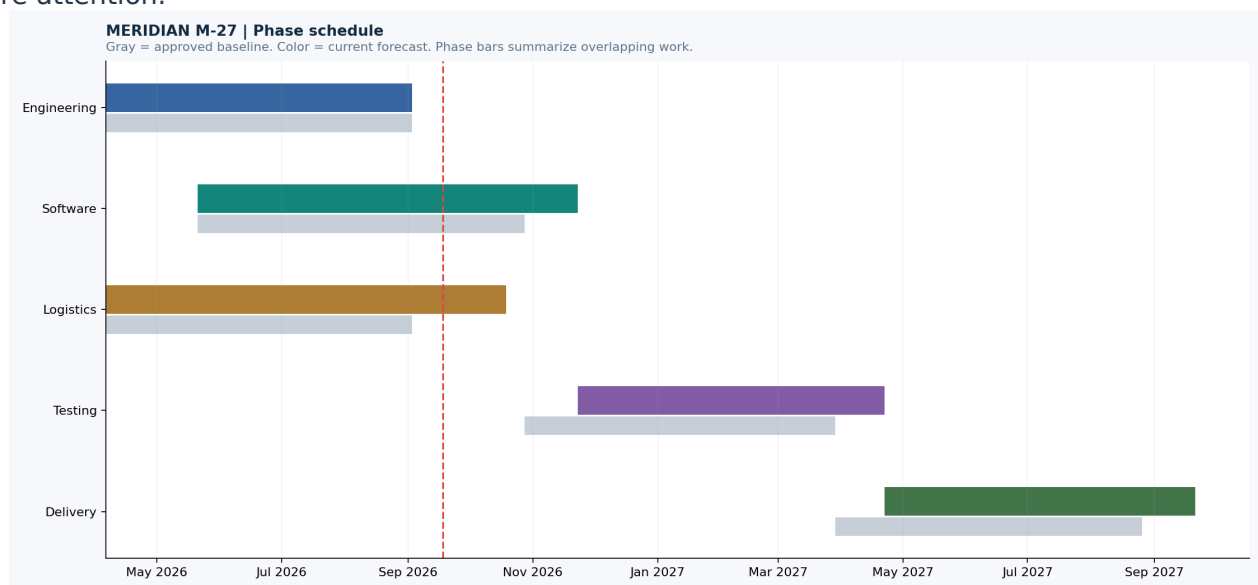


Management decisions

1. Review CR-002 before authorizing additional screening. Its duration impact remains outside the approved forecast.
2. Confirm coverage for overloaded resource pools. Publish a leveled recovery scenario before committing to a new acceptance date.
3. Preserve the original baseline. Record any future rebaseline as a separately approved version with an impact narrative.

Schedule quality: 6 of 14 screening indicators need review. Mixed SS/FF links are intentional but require engineering justification. 162 resource-days exceed capacity, totaling 153.0 excess FTE-days. These are capacity signals, not a computed delay estimate.

Risk and assurance findings

Status: 2026-09-18 | Fictional, unclassified portfolio demonstration

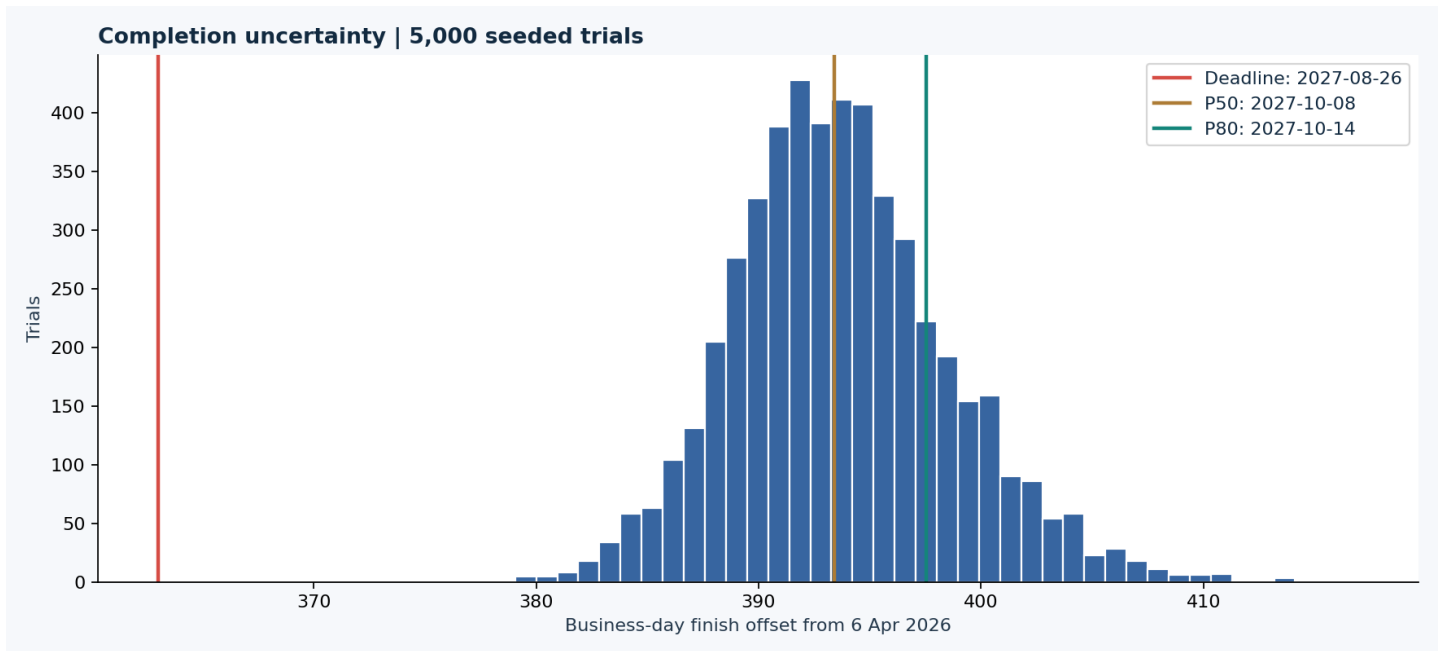

Highest expected task-level risks

Environmental retest: 30% probability, 10-35 conditional workdays. Owner: Test lead. Mitigation: Run prequalification screening before chamber booking.

Avionics interface rework: 35% probability, 8-30 conditional workdays. Owner: Software lead. Mitigation: Freeze interfaces and hold weekly integration reviews.

Ground test discrepancy: 40% probability, 5-22 conditional workdays. Owner: Test lead. Mitigation: Add an early dry run.

How to interpret the forecast

The model samples triangular remaining durations and Bernoulli risk occurrences. Actual starts and finishes remain fixed. Each trial reschedules the dependency network. P80 means 80% of simulated completions occur by that date under the stated assumptions. It is not a contractual confidence guarantee.

Limitations: No resource leveling, holidays, cost model or general duration correlation. Risk input ranges are fictional. Simulated impacts exclude already-realized issues in the current forecast. The 14-point screen uses documented demonstration thresholds and is not DCMA certification.

Method references: GAO-16-89G, best practices 6-10 and Appendix VII (gao.gov/products/gao-16-89g). See docs/METHODOLOGY.md for exact definitions, denominators and native-app validation limits.
